

LAB 2 – JIRA

Agile Backlog Creation & Sprint Simulation

1. Epics

The Lab 1 requirements were divided into five main Epics in Jira.

Epic	Name
SEL-1	Equipment Availability
SEL-2	Equipment Reservation
SEL-3	Equipment Calibration
SEL-4	Reservation & Double-Booking Management
SEL-5	Late Return & Disciplinary Management

Spaces

SELab2 ...

Summary List Board Backlog Development Forms Timeline Docs Reports +

Ask AI Search work Filter Group

	Work	Assignee	Reporter	Priority	Status	Resolution	Created
☐	> SEL-1 Equipment Availability	Unassigned	Pavithra Reddy	Medium	To Do	Unresolved	Aug 28, 2026, 3:02 PM
☐	> SEL-2 Equipment Reservation	Unassigned	Pavithra Reddy	Medium	To Do	Unresolved	Aug 28, 2026, 3:02 PM
☐	> SEL-3 Equipment Calibration	Unassigned	Pavithra Reddy	Medium	To Do	Unresolved	Aug 28, 2026, 3:04 PM
☐	> SEL-4 Reservation & Double-Booking Management	Unassigned	Pavithra Reddy	Medium	To Do	Unresolved	Aug 28, 2026, 3:05 PM
☐	> SEL-5 Late Return & Disciplinary Management	Unassigned	Pavithra Reddy	Medium	To Do	Unresolved	Aug 28, 2026, 3:05 PM

+ Create 5 of 5

Jira Epic list

2. User Stories and Story Points

The requirements were broken down into User Stories and Story Points were assigned to estimate the work.

Sprint	Stories	Story Points
Sprint 1	SEL-6 to SEL-15 (10 stories)	34
Sprint 2	SEL-16 to SEL-20 (5 stories)	24

The total work planned across the two sprints was 58 story points.

3. Sprint 1

Sprint 1 had 10 stories with 34 story points. The stories were moved from To Do to In Progress and then to Done.

SEL Sprint 1

31 Aug – 6 Sep (10 work items)

0

0


34

Complete sprint

...

SEL-6	View Real-Time Equipment Availability	Equipment Availabi...	Done	3		
SEL-7	View Available Time Slots	Equipment Availabi...	Done	2		
SEL-8	Reserve Equipment Slot	Equipment Reserv...	Done	5		
SEL-9	Enforce 2-Hour Reservation Limit	Equipment Reserv...	Done	3		
SEL-10	Allow Reservations Up to 7 Days in Advance	Equipment Reserv...	Done	2		
SEL-11	Generate Reservation Token	Equipment Reserv...	Done	3		
SEL-12	Check Equipment Calibration Status	Equipment Calibra...	Done	3		
SEL-13	Update Equipment Calibration Status	Equipment Calibra...	Done	3		
SEL-14	Prevent Reservation of Uncalibrated Equipment	Equipment Calibra...	Done	5		
SEL-15	Prevent Double-Booking	Reservation & Dou...	Done	5		

Sprint 1 board

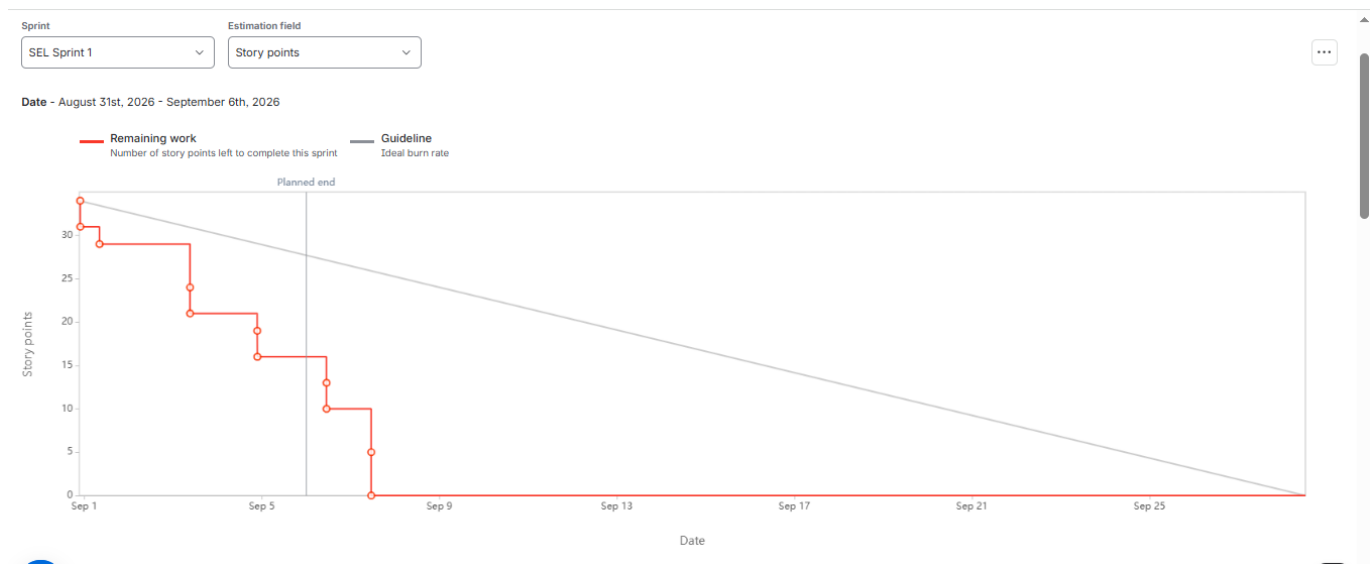


Sprint 1 Burndown Chart

4. Sprint 2

The remaining 5 stories were taken into Sprint 2. They had 24 story points in total and were completed.

Completed work items							View in All work navigator
Key	Summary	Work type	Epic	Status	Assignee	Story points	
SEL-16	Manage Equipment Reservations	Story	Reservation & Dou...	Done		5	
SEL-17	Handle Concurrent Reservation Requests	Story	Reservation & Dou...	Done		8	
SEL-18	Track Equipment Return Time	Story	Late Return & Disci...	Done		3	
SEL-19	Identify Late Equipment Returns	Story	Late Return & Disci...	Done		3	
SEL-20	Enforce Late-Return Disciplinary Rules	Story	Late Return & Disci...	Done		5	


Sprint 2 completed work

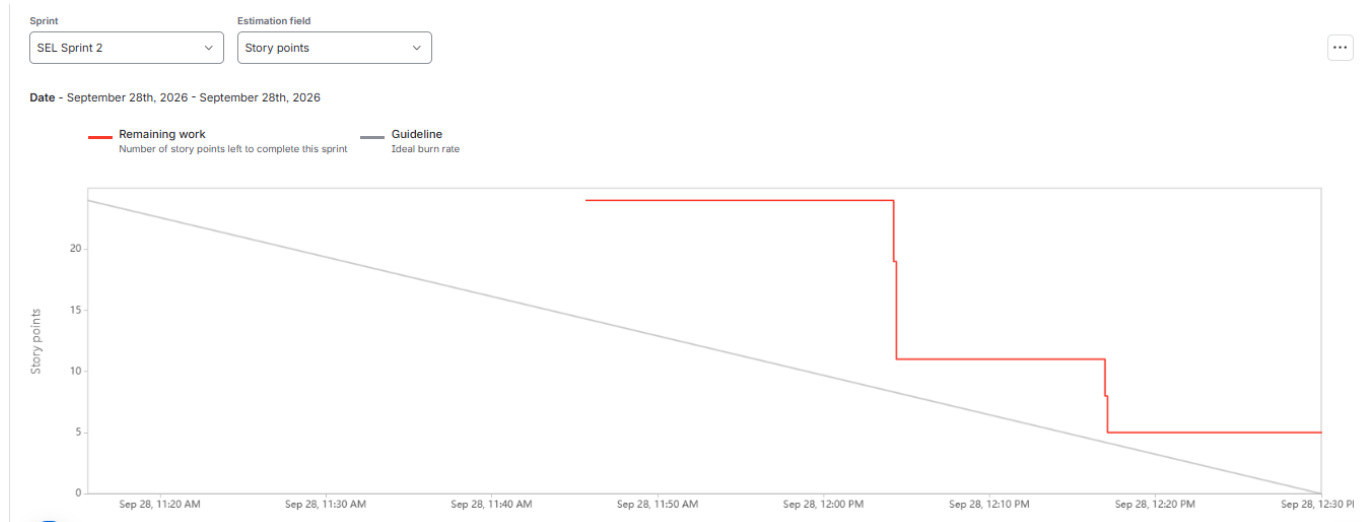

Sprint 2 Burndown Chart

5. Final Backlog

After completing both sprints, there were no remaining items in the backlog.

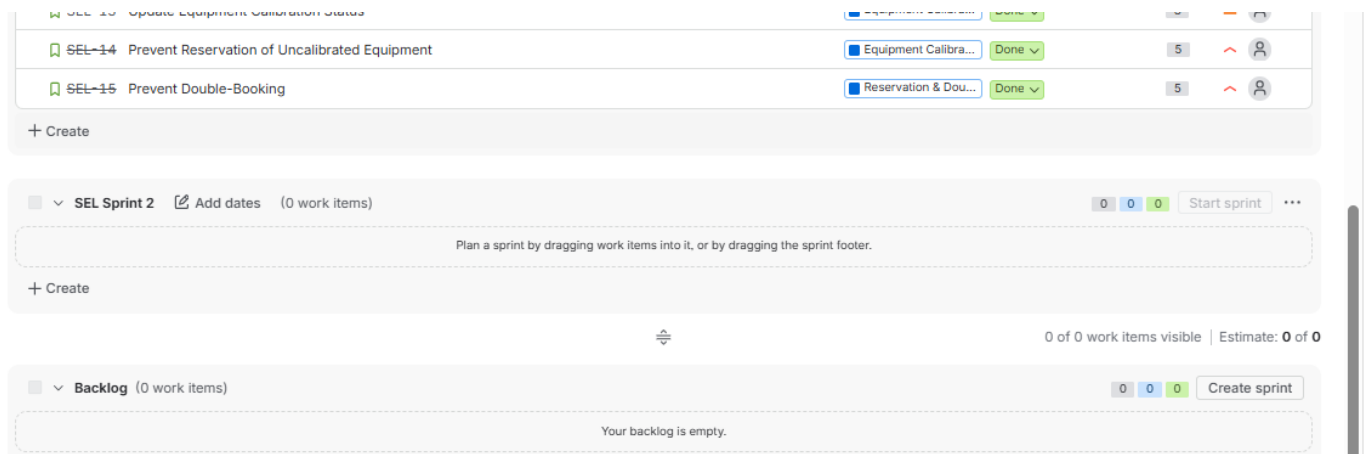

Final Jira backlog

6. Reflection

1. Did your estimations reflect the actual effort?

Mostly yes. The smaller tasks had fewer story points and the more complicated reservation and concurrency tasks had higher points. The stories were completed within the two simulated sprints.

2. Was your backlog well-prioritized?

Yes. The basic availability and reservation work was taken first in Sprint 1. The remaining reservation management and late-return work was done in Sprint 2.

3. How did your simulated sprint align with your plan?

The work was divided into two sprints. Sprint 1 covered the main reservation and calibration features, and Sprint 2 covered the remaining reservation and late-return features. All the selected stories were completed.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed how the remaining story points went down as the stories were completed. Sprint 1 started with 34 points and Sprint 2 started with 24 points, and both reached zero.
